

USAGE REPORT

Vehicle: SRBC TEST

Date: 05/03/2026

Location: Valence

Missions: 2

Mission 1

Trial date 2026-03-05

Location Valence, Drome, France

Operator Nicolas

Start time 18:20

End time 18:28

Weather

Precipitation type None

Temperature 16 °C

Sun position Couché

Terrain

Slope 3 %

Cross slope 7 %

Soil

Texture Clay loam

Dominant particle size Gravel 2-20 mm

Moisture condition Friable (optimal)

Crop

Growth stage Soil preparation

Weed pressure 0 %

Planned operation Soil preparation

Adjacent environment

Tall vegetation No

Tall buildings No

Metallic structures Yes

Ditch or embankment No

High voltage lines No

Roads No

No network zone	No
Robot configuration	
Robot weight	280 kg
Robot width	0.64 m
<i>Tool</i>	
Tool name	Herse etri
Tool type	Mounted
Tool weight	30 kg
Tool length	0.8 m
Tool width	0.6 m
Tool height	0.6 m
Tool total length	1.1 m
Working depth	0.04 m



Figure 1.1: Mission presentation photo

Mission presentation

Mission parameters

Task to perform	grattage
Trajectory	rectiligne, square turn
Working speed	2.8 km/h
Mission file	Valencechenillard3.json

Organization

<i>Workforce</i>	
Total number of employees	2
Employees on robot task	0
<i>Surface</i>	
	0.03 ha

Theoretical surface of the plot

Worked plot surface 0.0152 ha

Plot fragmentation Consolidated (<0.5 km)

Trajectory

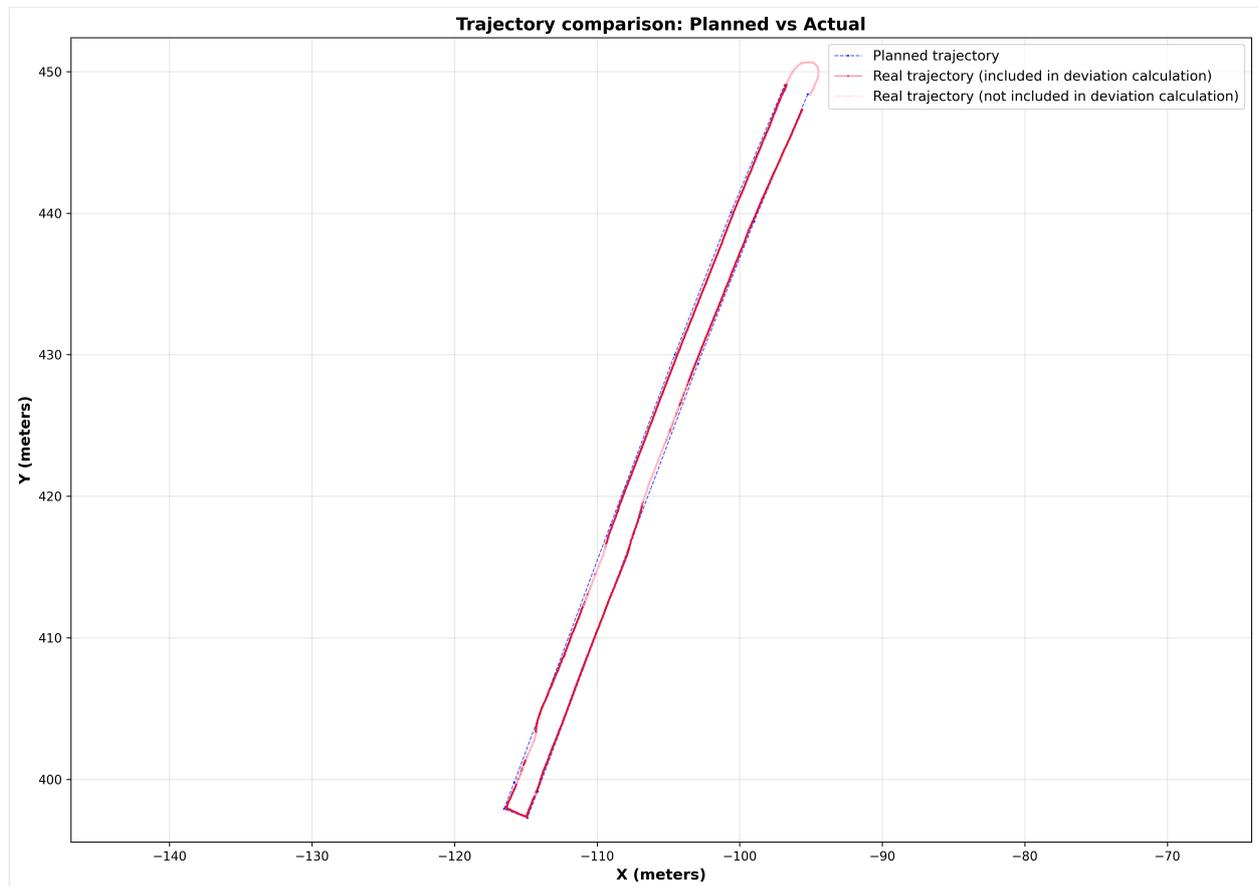


Figure 1.1: Planned vs actual trajectory comparison

Agronomic Summary

Energy per hectare 6.05 kWh/ha

Work rate 0.07 ha/h

Autonomy per battery 0.42 ha/batterie

Time tracking

Tool setup 1 min

GPS connection wait 0 min

Wi-Fi connection wait 0 min

Supervision time 10 min

Travel time 1 min

Restart count 0

Stop count	4
Stop causes	probleme de suivis derive
Work assessment	
Quality assessment	Neutral
Crop damage	None

Performance Indicators

Agronomic ^[1]

Indicateur	Valeur	Unité
Crop species	<i>N/A</i>	
Growth stage	Soil preparation	
Soil texture	Clay loam	
Soil moisture	Friable (optimal)	
Weed pressure	0	%
Planned operation	Soil preparation	
Work quality assessment	Neutral	
Crop damage	None	

Energy ^[2]


Indicateur	Valeur	Unité
SOC at start	95.70	%
SOC at end	93.80	%
Total discharge ^[3] <i>For a battery pack capacity of: 2.54 kWh</i>	2.05	%
Total energy consumed	0.05	kWh
Average power	0.45	kW
Energy per hectare	6.05	kWh/ha
Autonomy per battery <i>Reference battery: 2.54 kWh</i>	0.42	ha/batterie

Work Rate ^[4]

Indicateur	Valeur	Unité
Work rate ^[5]	0.07	ha/h
Area covered ^[6]	0.01	ha

Indicateur	Valeur	Unité
Worked plot surface ^[7]	0.02	ha
Worked area ^[8]	0.01	ha
Effective area ^[9]	0.01	ha
Coverage rate ^[10]	0.00	%
Average speed (km/h)	1.03	km/h
Max speed (km/h)	2.18	km/h

Trajectory with tools down and worked area

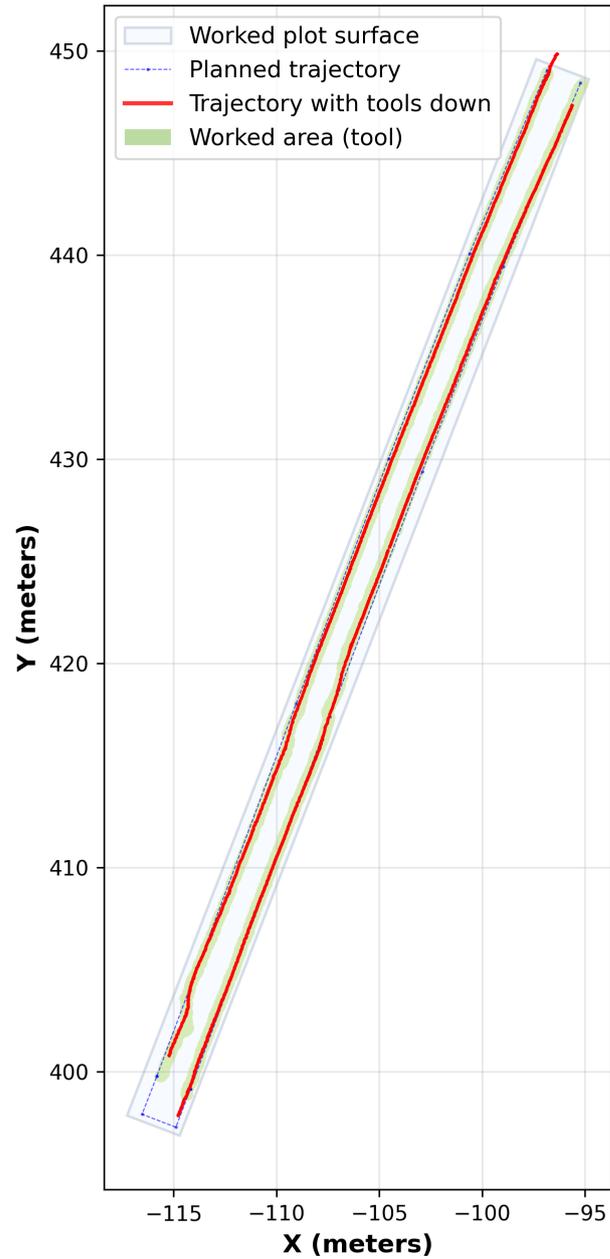

1

Nombre de recouvrements

Economic ^[11]

Indicateur	Valeur	Unité
Electricity price	N/A	€/kWh
Labor cost per hour	N/A	€/h
Employees assigned	0	
Labor cost per hectare	N/A	€/ha

Indicateur	Valeur	Unité
Energy cost	<i>N/A</i>	€
Energy cost per hectare	<i>N/A</i>	€/ha
Total cost <i>Prix de l'électricité non disponible dans le COD</i>	<i>N/A</i>	€
Total cost per hectare	<i>N/A</i>	€/ha

Environmental ^[12]

Indicateur	Valeur	Unité
Temperature	16	°C
Precipitation type	None	
CO ₂ emissions ^[13] <i>Emission factor applied: 317 g CO₂ per kWh.</i>	0.02	kg
Plot fragmentation	Consolidated (<0.5 km)	

Mission ^[14]

Indicateur	Valeur	Unité
Planned distance ^[15]	111.36	m
Performed distance ^[16]	134.94	m
Distance deviation	23.58	m
Performed distance (%)	121.17	%
Mean lateral deviation <i>Without half-turn</i>	10.94	cm
Max lateral deviation <i>Without half-turn</i>	20.00	cm
Mean lateral deviation (tool) <i>Without half-turn, tool distance: 110 cm</i>	11.53	cm
Max lateral deviation (tool) <i>Without half-turn, tool distance: 110 cm</i>	20.00	cm
Worked rows ^[17]	2	

Operational ^[18]

Indicateur	Valeur	Unité
Robot weight	280.00	kg
Tool weight	<i>N/A</i>	kg
Total weight	280.00	kg
Energy per kg per hectare	0.02	kWh/kg/ha

Indicateur	Valeur	Unité
Mean torque at work (% of nominal) ^[19] <i>Reference nominal torque: 2.39 N·m — Number of motors: 2.</i>	59.15	%

Safety ^[20]

Indicateur	Valeur	Unité
Geofencing exits	0	
Time outside geofencing (seconds)	0.00	s
Time outside geofencing (hours)	0.00	h
Local emergency stops	0	
Remote emergency stops	0	
Bumper activations	0	

Reliability ^[21]

Indicateur	Valeur	Unité
Output errors	0	
Input errors	0	
Battery errors	0	
Motor errors	0	
Cylinder errors	0	
Total errors	0	
Output error time (seconds)	0.00	s
Input error time (seconds)	0.00	s
Battery error time (seconds)	0.00	s
Motor error time (seconds)	0.00	s
Cylinder error time (seconds)	0.00	s
Total error time (seconds)	0.00	s
Error rate per hour	0.00	/h
System availability	100.00	%

Localization ^[22]

Indicateur	Valeur	Unité
Localization errors	0	
Error time (seconds)	0.00	s
Error time (hours)	0.00	h

Time ^[23]

Indicateur	Valeur	Unité
Total duration	424.50	s
Total duration (hours)	0.12	h
Active time	312.69	s
Active time (hours)	0.09	h
Inactive time	111.81	s
Inactive time (hours)	0.03	h
Active time (%)	73.66	%
Inactive time (%)	26.34	%

Mission 2

Trial date	2026-03-05
Location	Valence, Drome, France
Operator	Nicolas
Start time	18:29
End time	18:58

Weather

Precipitation type	None
Temperature	16 °C
Sun position	Couché

Terrain

Slope	3 %
Cross slope	7 %

Soil

Texture	Clay loam
Dominant particle size	Gravel 2-20 mm
Moisture condition	Friable (optimal)

Crop

Growth stage	Soil preparation
Weed pressure	0 %
Planned operation	Soil preparation

Adjacent environment

Tall vegetation	No
Tall buildings	No
Metallic structures	Yes
Ditch or embankment	No
High voltage lines	No
Roads	No
No network zone	No

Robot configuration

Robot weight	280 kg
Robot width	0.64 m

Tool

Tool name	Herse etri
Tool type	Mounted
Tool weight	30 kg
Tool length	0.8 m
Tool width	0.6 m
Tool height	0.6 m
Tool total length	1.1 m
Working depth	0.04 m



Figure 2.1: Mission presentation photo

Mission presentation

Mission parameters

Task to perform	grattage
Trajectory	rectiligne, square turn
Working speed	2.8 km/h
Mission file	Valencechenillard2.json

Organization

Workforce

Total number of employees	2
Employees on robot task	0

Surface

Theoretical surface of the plot	0.03 ha
Worked plot surface	0.0192 ha
Plot fragmentation	Consolidated (<0.5 km)

Trajectory

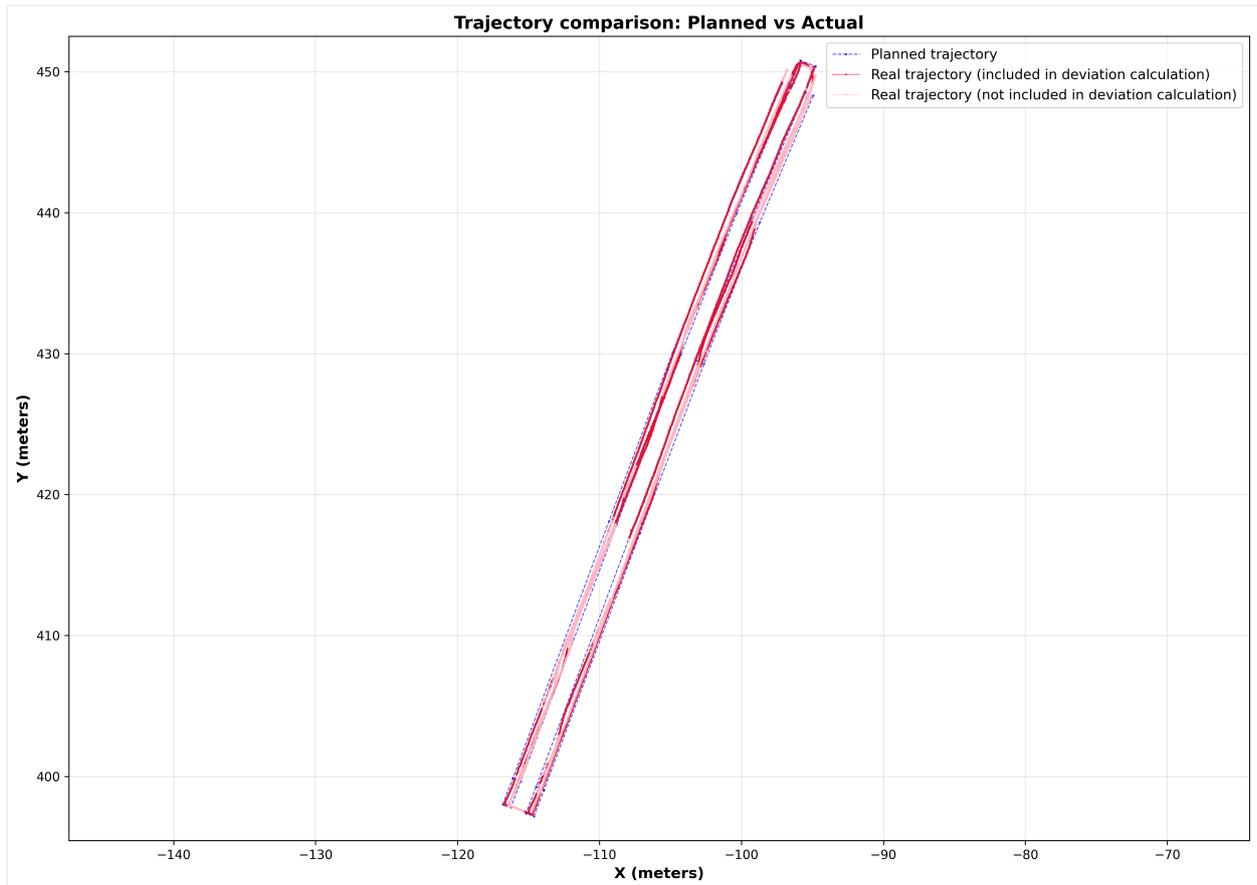


Figure 2.1: Planned vs actual trajectory comparison

Agronomic Summary

Energy per hectare	5.09 kWh/ha
Work rate	0.07 ha/h
Autonomy per battery	0.50 ha/batterie

Time tracking

Tool setup	0 min
GPS connection wait	0 min
Wi-Fi connection wait	0 min
Supervision time	80 min
Travel time	5 min
Restart count	0
Stop count	10
Stop causes	probleme de suivis derive; redemarrage loc changement de base

Work assessment

Quality assessment	Neutral
--------------------	---------

Crop damage

None

Performance Indicators

Agronomic ^[1]

Indicateur	Valeur	Unité
Crop species	N/A	
Growth stage	Soil preparation	
Soil texture	Clay loam	
Soil moisture	Friable (optimal)	
Weed pressure	0	%
Planned operation	Soil preparation	
Work quality assessment	Neutral	
Crop damage	None	

Energy ^[2]


Indicateur	Valeur	Unité
SOC at start	93.80	%
SOC at end	87.30	%
Total discharge ^[3] <i>For a battery pack capacity of: 2.54 kWh</i>	6.85	%
Total energy consumed	0.17	kWh
Average power	0.35	kW
Energy per hectare	5.09	kWh/ha
Autonomy per battery <i>Reference battery: 2.54 kWh</i>	0.50	ha/batterie

Work Rate ^[4]

Indicateur	Valeur	Unité
Work rate ^[5]	0.07	ha/h
Area covered ^[6]	0.03	ha
Worked plot surface ^[7]	0.02	ha
Worked area ^[8]	0.03	ha
Effective area ^[9]	0.01	ha
Coverage rate ^[10]	129.83	%

Indicateur	Valeur	Unité
Average speed (km/h)	1.10	km/h
Max speed (km/h)	2.72	km/h

Trajectory with tools down and worked area

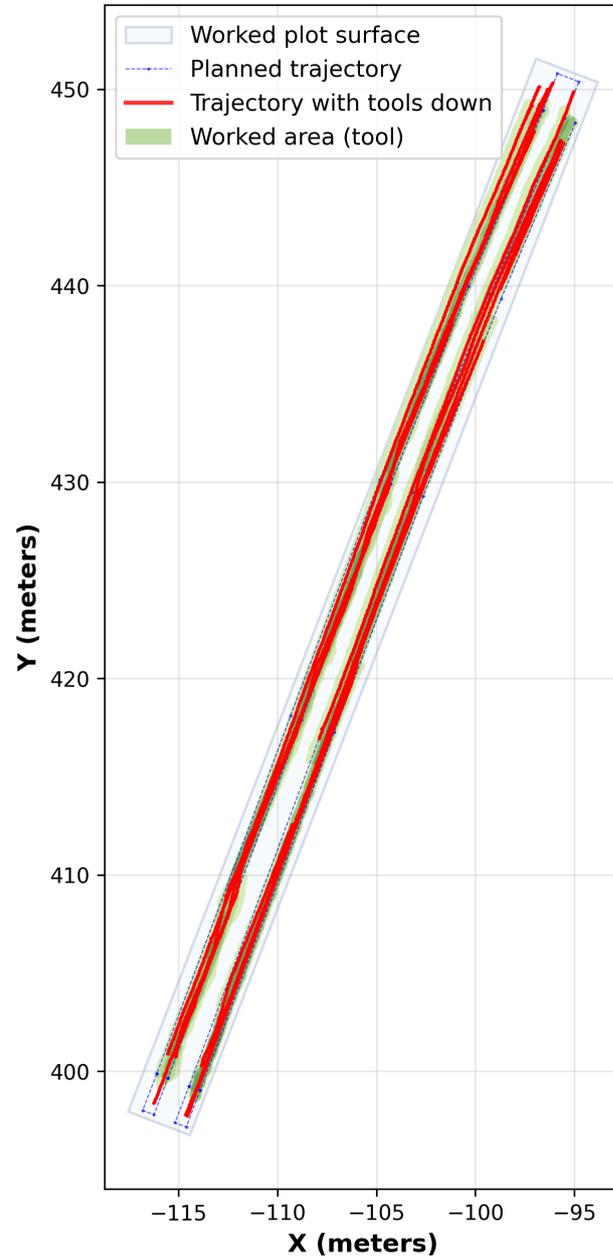

Economic ^[11]

Indicateur	Valeur	Unité
Electricity price	N/A	€/kWh

Indicateur	Valeur	Unité
Labor cost per hour	N/A	€/h
Employees assigned	0	
Labor cost per hectare	N/A	€/ha
Energy cost	N/A	€
Energy cost per hectare	N/A	€/ha
Total cost <i>Prix de l'électricité non disponible dans le COD</i>	N/A	€
Total cost per hectare	N/A	€/ha

Environmental ^[12]

Indicateur	Valeur	Unité
Temperature	16	°C
Precipitation type	None	
CO ₂ emissions ^[13] <i>Emission factor applied: 317 g CO₂ per kWh.</i>	0.06	kg
Plot fragmentation	Consolidated (<0.5 km)	

Mission ^[14]

Indicateur	Valeur	Unité
Planned distance ^[15]	225.59	m
Performed distance ^[16]	535.04	m
Distance deviation	309.45	m
Performed distance (%)	237.17	%
Mean lateral deviation <i>Without half-turn</i>	10.78	cm
Max lateral deviation <i>Without half-turn</i>	20.00	cm
Mean lateral deviation (tool) <i>Without half-turn, tool distance: 110 cm</i>	11.14	cm
Max lateral deviation (tool) <i>Without half-turn, tool distance: 110 cm</i>	20.00	cm
Worked rows ^[17]	4	

Operational ^[18]

Indicateur	Valeur	Unité
Robot weight	280.00	kg

Indicateur	Valeur	Unité
Tool weight	<i>N/A</i>	kg
Total weight	280.00	kg
Energy per kg per hectare	0.02	kWh/kg/ha
Mean torque at work (% of nominal) ^[19] <i>Reference nominal torque: 2.39 N·m — Number of motors: 2.</i>	50.88	%

Safety ^[20]

Indicateur	Valeur	Unité
Geofencing exits	0	
Time outside geofencing (seconds)	0.00	s
Time outside geofencing (hours)	0.00	h
Local emergency stops	0	
Remote emergency stops	0	
Bumper activations	0	

Reliability ^[21]

Indicateur	Valeur	Unité
Output errors	0	
Input errors	0	
Battery errors	0	
Motor errors	0	
Cylinder errors	0	
Total errors	0	
Output error time (seconds)	0.00	s
Input error time (seconds)	0.00	s
Battery error time (seconds)	0.00	s
Motor error time (seconds)	0.00	s
Cylinder error time (seconds)	0.00	s
Total error time (seconds)	0.00	s
Error rate per hour	0.00	/h
System availability	100.00	%

Localization [22]

Indicateur	Valeur	Unité
Localization errors	0	
Error time (seconds)	0.00	s
Error time (hours)	0.00	h

Time [23]

Indicateur	Valeur	Unité
Total duration	1773.16	s
Total duration (hours)	0.49	h
Active time	1334.91	s
Active time (hours)	0.37	h
Inactive time	438.25	s
Inactive time (hours)	0.12	h
Active time (%)	75.28	%
Inactive time (%)	24.72	%

Descriptions of indicators

Bracketed numbers refer to definitions, assumptions and sources listed below.

- [1] Agronomic indicator: value from the recorded crop trial context.
- [2] Energy indicator: derived from electrical measurements, consumption and SOC logged during the mission.
- [3] Total discharge (%): energy consumed during the mission (change in cumulative energy, in kWh) divided by nominal battery pack capacity (kWh), multiplied by 100. This indicator does not use start or end SOC; reference pack capacity is stated in the note when known.
- [4] Work-rate indicator: derived from worked areas, speeds and time on field.
- [5] Work rate: amount of work completed per unit of time, in ha/h. Hourly rate = area covered (ha) ÷ total mission duration (h).
- [6] Area covered: this is the area swept by the robot = cumulative odometric distance × robot width.
- [7] Worked plot surface: area of the plot worked by the robot. It is modeled as an oriented bounding box (OBB) with a margin equal to half the robot width around the planned trajectory that was worked.
- [8] Worked area: area processed by the implement (tool width × path length with implement lowered). Each pass counts; overlaps add up.
- [9] Effective area: area worked by the implement excluding overlaps.
- [10] Coverage rate: ratio of worked area to effective area. $(\text{worked area} - \text{effective area}) / \text{effective area} \times 100$. A high value indicates many passes over the same zones.
- [11] Economic indicator: computed from cost settings and mission energy/time aggregates.
- [12] Environmental indicator: derived from weather context or consumption using the documented method.
- [13] CO₂ emissions from grid electricity consumed during the mission (kWh × 0.317 kg/kWh). Source: French Ministry for Ecological Transition — Key Climate Figures (digital edition), chapter on GHG emissions from industry / electricity production (statistiques.developpement-durable.gouv.fr).
- [14] Mission indicator: derived from actual path, plan and computed geometric deviations.
- [15] Theoretical mission distance: cumulative length of the planned trajectory from the mission JSON file. Does not match the robot's actual path.
- [16] Distance actually traveled by the robot. May include movement before the mission effectively starts and after it ends, depending on the recorded data.
- [17] Number of distinct rows worked (tool lowered).
- [18] Operational indicator: derived from kinematics, implement data or documented masses.
- [19] Mean absolute motor torque only when the tool is lowered, as a percentage of the motors' nominal torque.
- [20] Safety indicator: derived from safety-related events and durations.
- [21] Reliability indicator: derived from fault codes and error time per subsystem.
- [22] Localization indicator: derived from localization faults or downtime during the mission.
- [23] Time indicator: derived from timestamps and activity states during the mission.
